



ID	Task Mode	Task Name	Duration	Start	Finish			02 Sep '19							09 Sep '19							16 Sep '19							23 Sep '19							30
						S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
41	➡	Carry out Positive Isolation of Process Connec	1 day?	Sat 14/12/19	Sun 15/12/19																															
42	➡	Open Contactor Manholes	1 day?	Sun 15/12/19	Mon 16/12/19																															
43	➡	Flush & Drain Residual HC from Contactor	1 day?	Mon 16/12/19	Tue 17/12/19																															
44	➡	Install Air Blowers	1 day?	Tue 17/12/19	Wed 18/12/19																															
45	➡	Inspect Inlet Device, Lower Mist Eliminator &	1 day?	Tue 17/12/19	Wed 18/12/19																															
46	➡	Remove Feed Inlet Piping	1 day?	Wed 18/12/19	Thu 19/12/19																															
47	➡	Remove Existing Liquid Distributor above Pack	1 day?	Thu 19/12/19	Fri 20/12/19																															
48	➡	Remove Existing Upper Mist Eliminator	1 day?	Fri 20/12/19	Sat 21/12/19																															
49	➡	Remove Existing Packing	1 day?	Sat 21/12/19	Sun 22/12/19																															
50	➡	Install Expansion Rings for Odd & Even Turbo	1 day?	Sun 22/12/19	Sun 22/12/19																															
51	➡	Install Expansion Rings for Secondary & Prima	1 day?	Mon 23/12/19	Mon 23/12/19																															
52	➡	Install Odd & Even Turbo Trays on Expansion F	3 days	Tue 24/12/19	Thu 26/12/19																															
53	➡	Install Secondary Mist Elimnator on Expansion	1 day?	Fri 27/12/19	Fri 27/12/19																															
54	➡	Install Support for Versi-Swirl	1 day?	Sat 28/12/19	Sat 28/12/19																															
55	➡	Install Versi-Swirl Deck	1 day?	Sat 28/12/19	Sun 29/12/19																															
56	➡	Install Primary Mist Eliminator on Expansion R	1 day?	Sun 29/12/19	Mon 30/12/19																															
57	➡	Install Feed Inlet Piping	1 day?	Mon 30/12/19	Tue 31/12/19																															
58	➡	Conduct Final Inspection before Box-up	1 day?	Tue 31/12/19	Wed 01/01/20																															
59	➡	Remove Blower	1 day?	Wed 01/01/20	Thu 02/01/20																															
60	➡	Close Contactor Manholes	1 day?	Thu 02/01/20	Fri 03/01/20																															
61	➡	Reverse Positive Isolation on Contactor	1 day?	Fri 03/01/20	Sat 04/01/20																															
62	➡	Torque all Disturbed Joints	1 day?	Fri 03/01/20	Sat 04/01/20																															
63	➡	Carry out Nitrogen Purging and Leak Test	1 day?	Sat 04/01/20	Sun 05/01/20																															
64	➡	Sign off SOF	1 day?	Tue 07/01/20	Wed 08/01/20																															
65	➡	Conduct Line Walk	1 day?	Wed 08/01/20	Thu 09/01/20																															
66	➡	Deisolate Contactor	1 day?	Wed 08/01/20	Thu 09/01/20																															
67	➡	Dismantle Scaffold	5 days	Fri 10/01/20	Wed 15/01/20																															
68	➡	Clean up Site	1 day?	Wed 15/01/20	Thu 16/01/20																															
69	➡	Demobilize Contractor	2 days	Thu 16/01/20	Sat 18/01/20																															
70	➡	Commissioning & Start Up	51.25 days?	Fri 01/11/19	Mon 13/01/20																															
71	➡	Engage CSU Team on Project	1 day?	Fri 01/11/19	Fri 01/11/19																															
72	➡	Prepare A & B Checksheets	15 days	Mon 04/11/19	Fri 22/11/19																															
73	➡	Complete A Checksheets	5 days	Mon 30/12/19	Sat 04/01/20																															
74	➡	Issue Mechanical Completion Certificate	1 day?	Sat 04/01/20	Sun 05/01/20																															
75	➡	Complete B Checksheets	1 day?	Sun 05/01/20	Mon 06/01/20																															
76	➡	Issue Precommissioning Completion Certificat	1 day?	Mon 06/01/20	Tue 07/01/20																															
77	➡	Issue RFSU Certificate	1 day?	Mon 06/01/20	Tue 07/01/20																															
78	➡	Start up	1 day?	Thu 09/01/20	Fri 10/01/20																															
79	➡	Carry out 72 Hr Run Test	3 days	Fri 10/01/20	Mon 13/01/20																															

Project: Soku Turbo Trays Insta  
Date: Wed 09/10/19

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone


Deadline

Progress


Manual Progress

Page 2

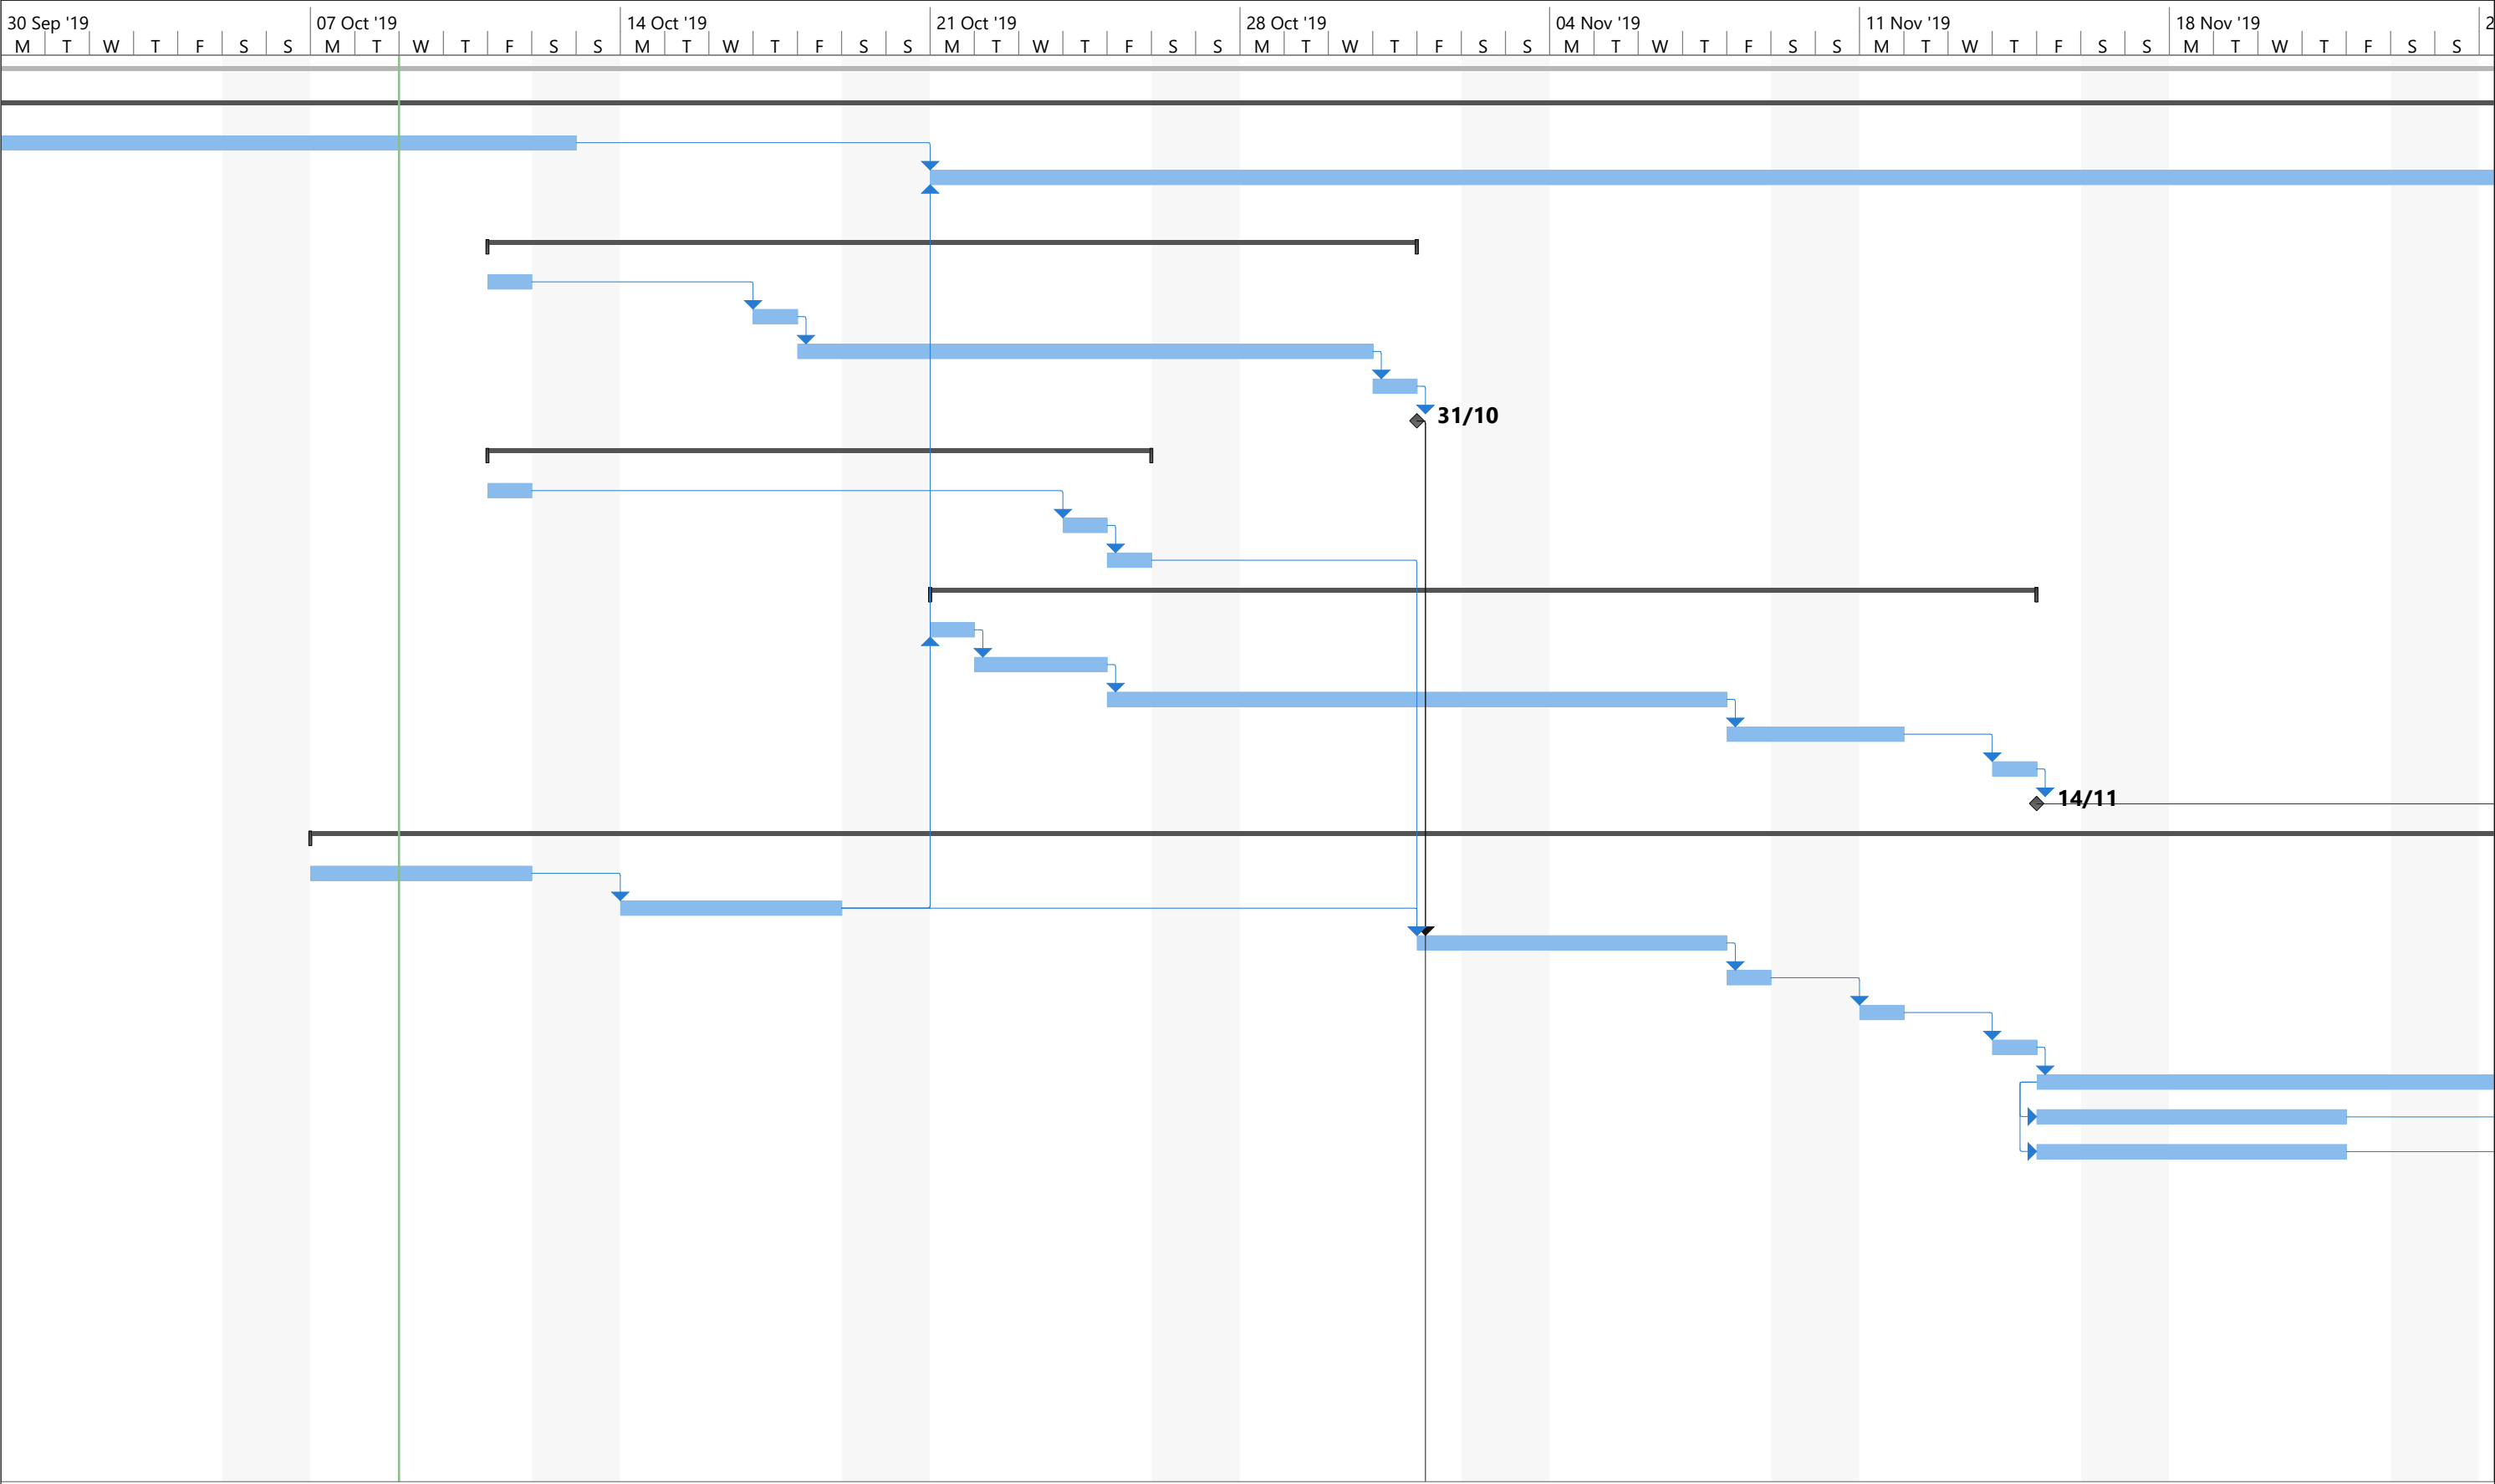

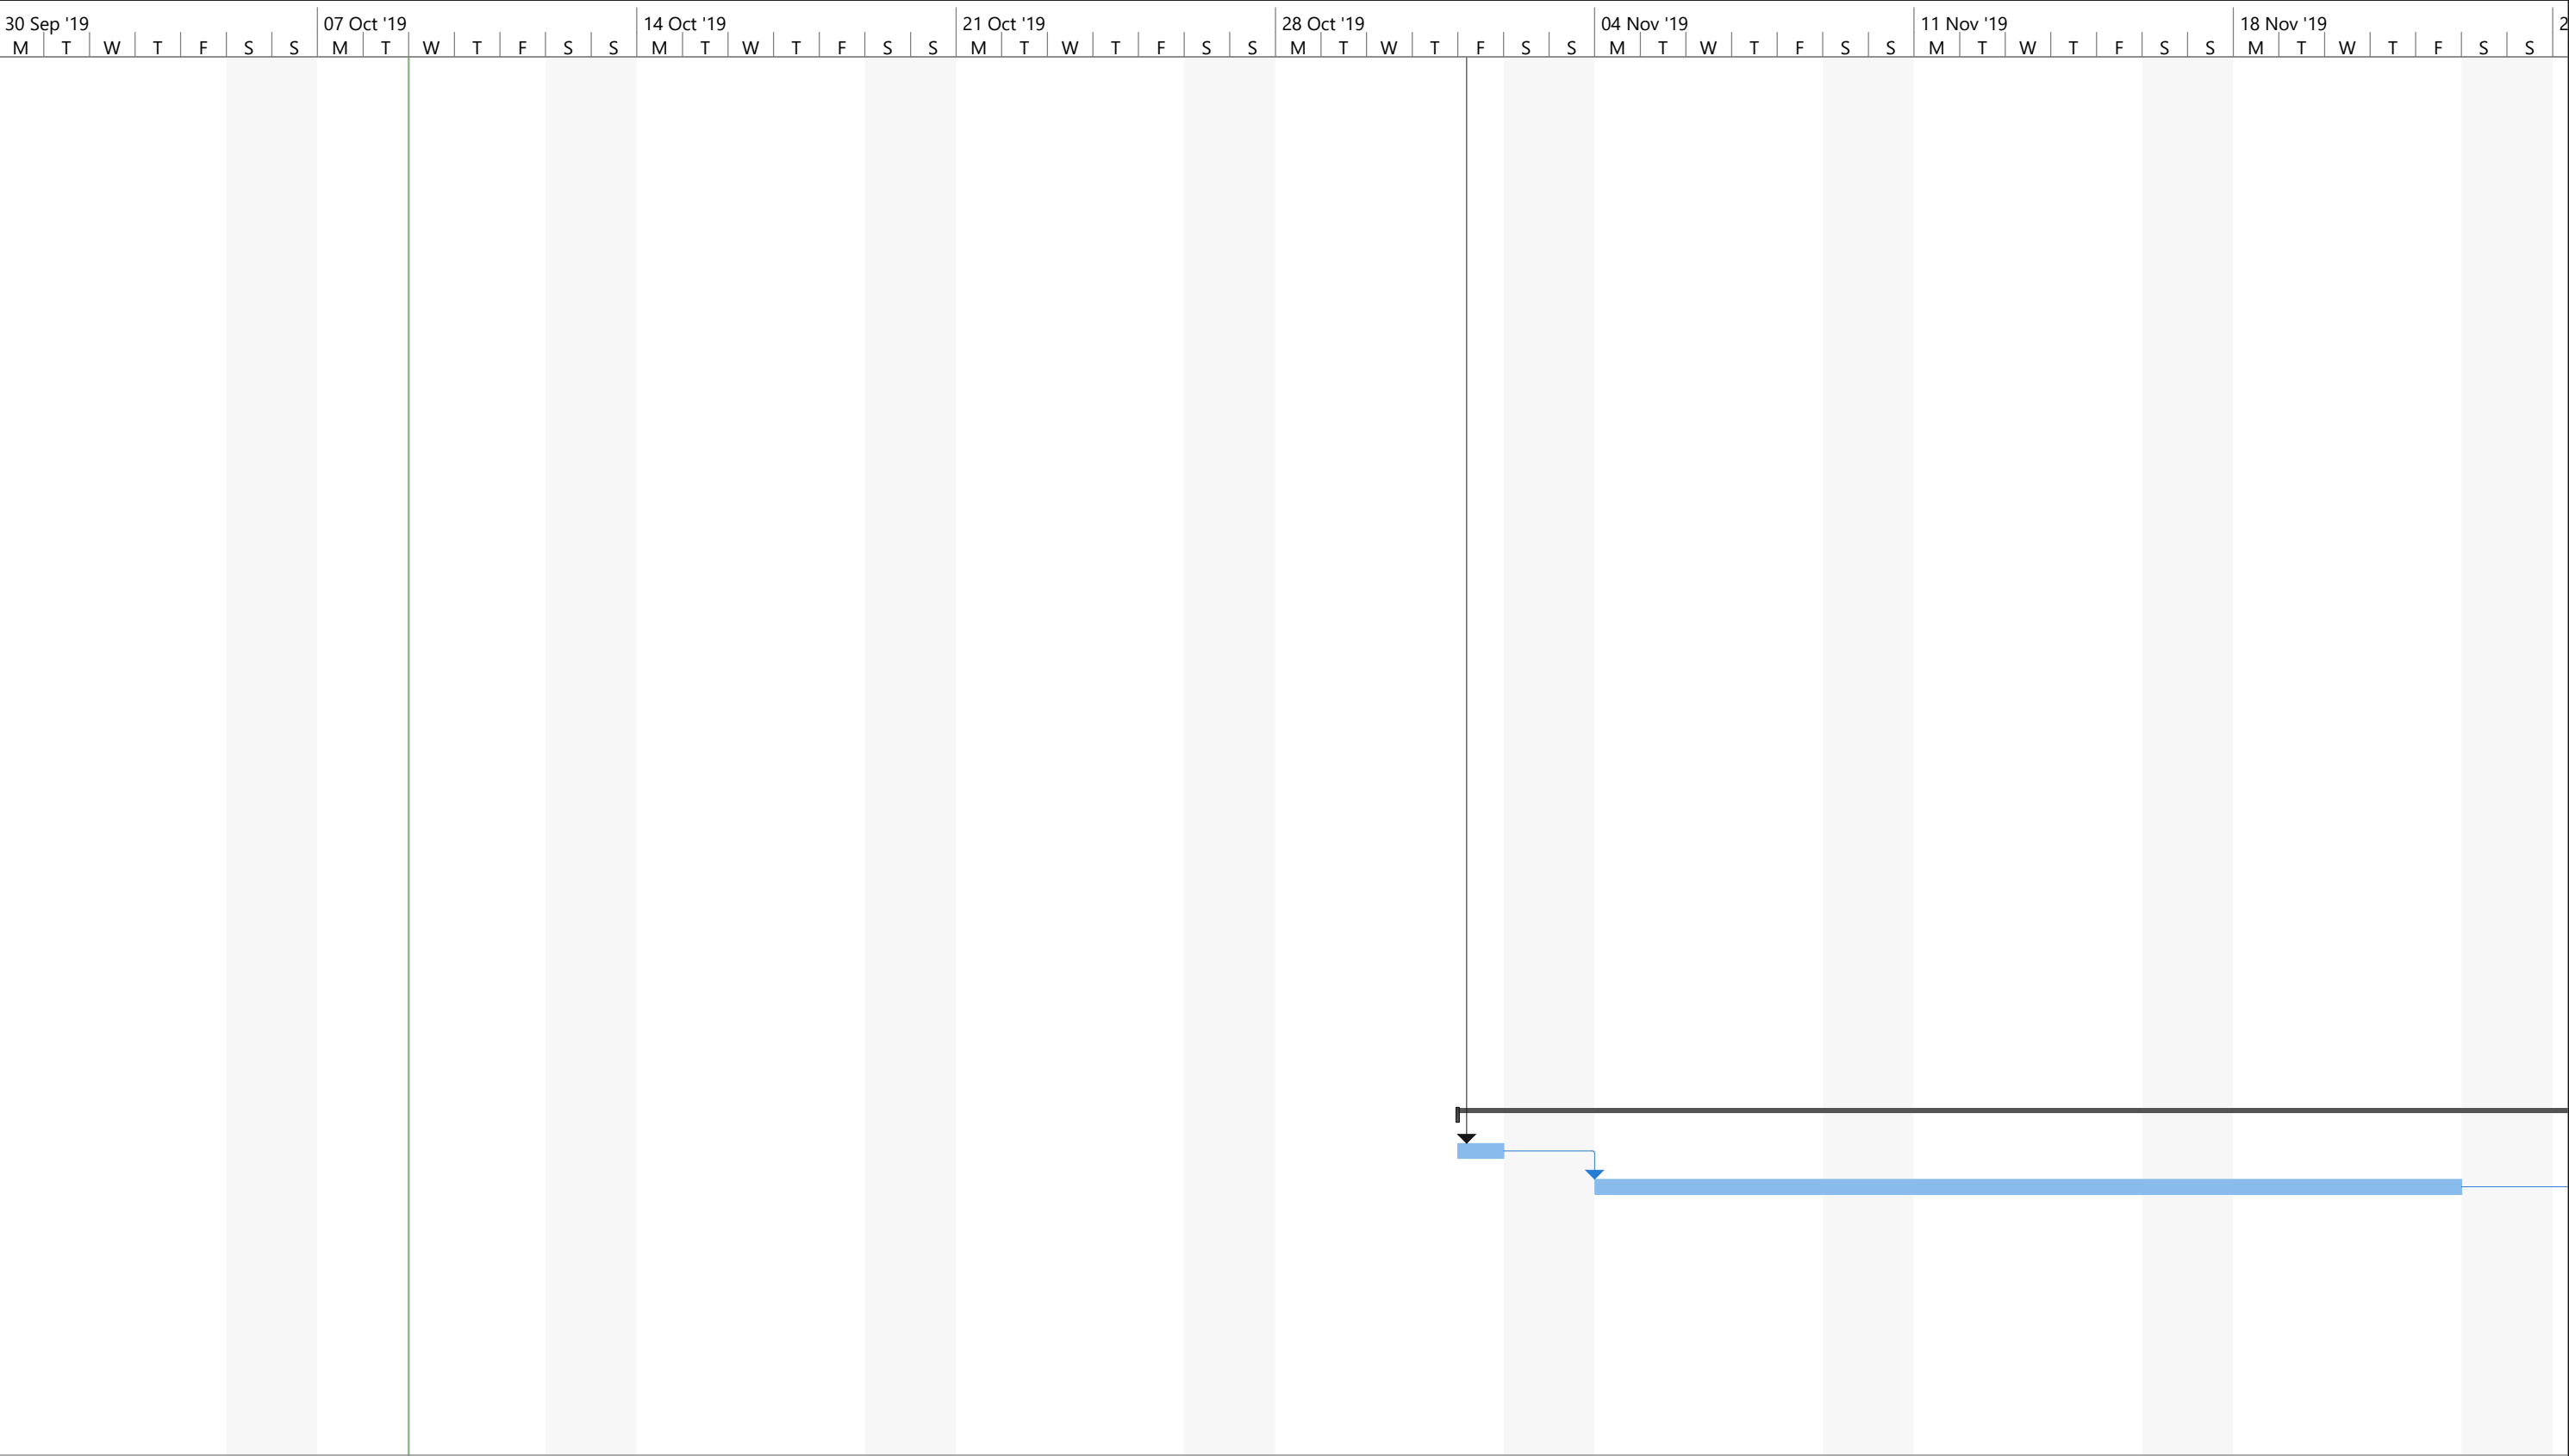

Project: Soku Turbo Trays Insta Date: Wed 09/10/19	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

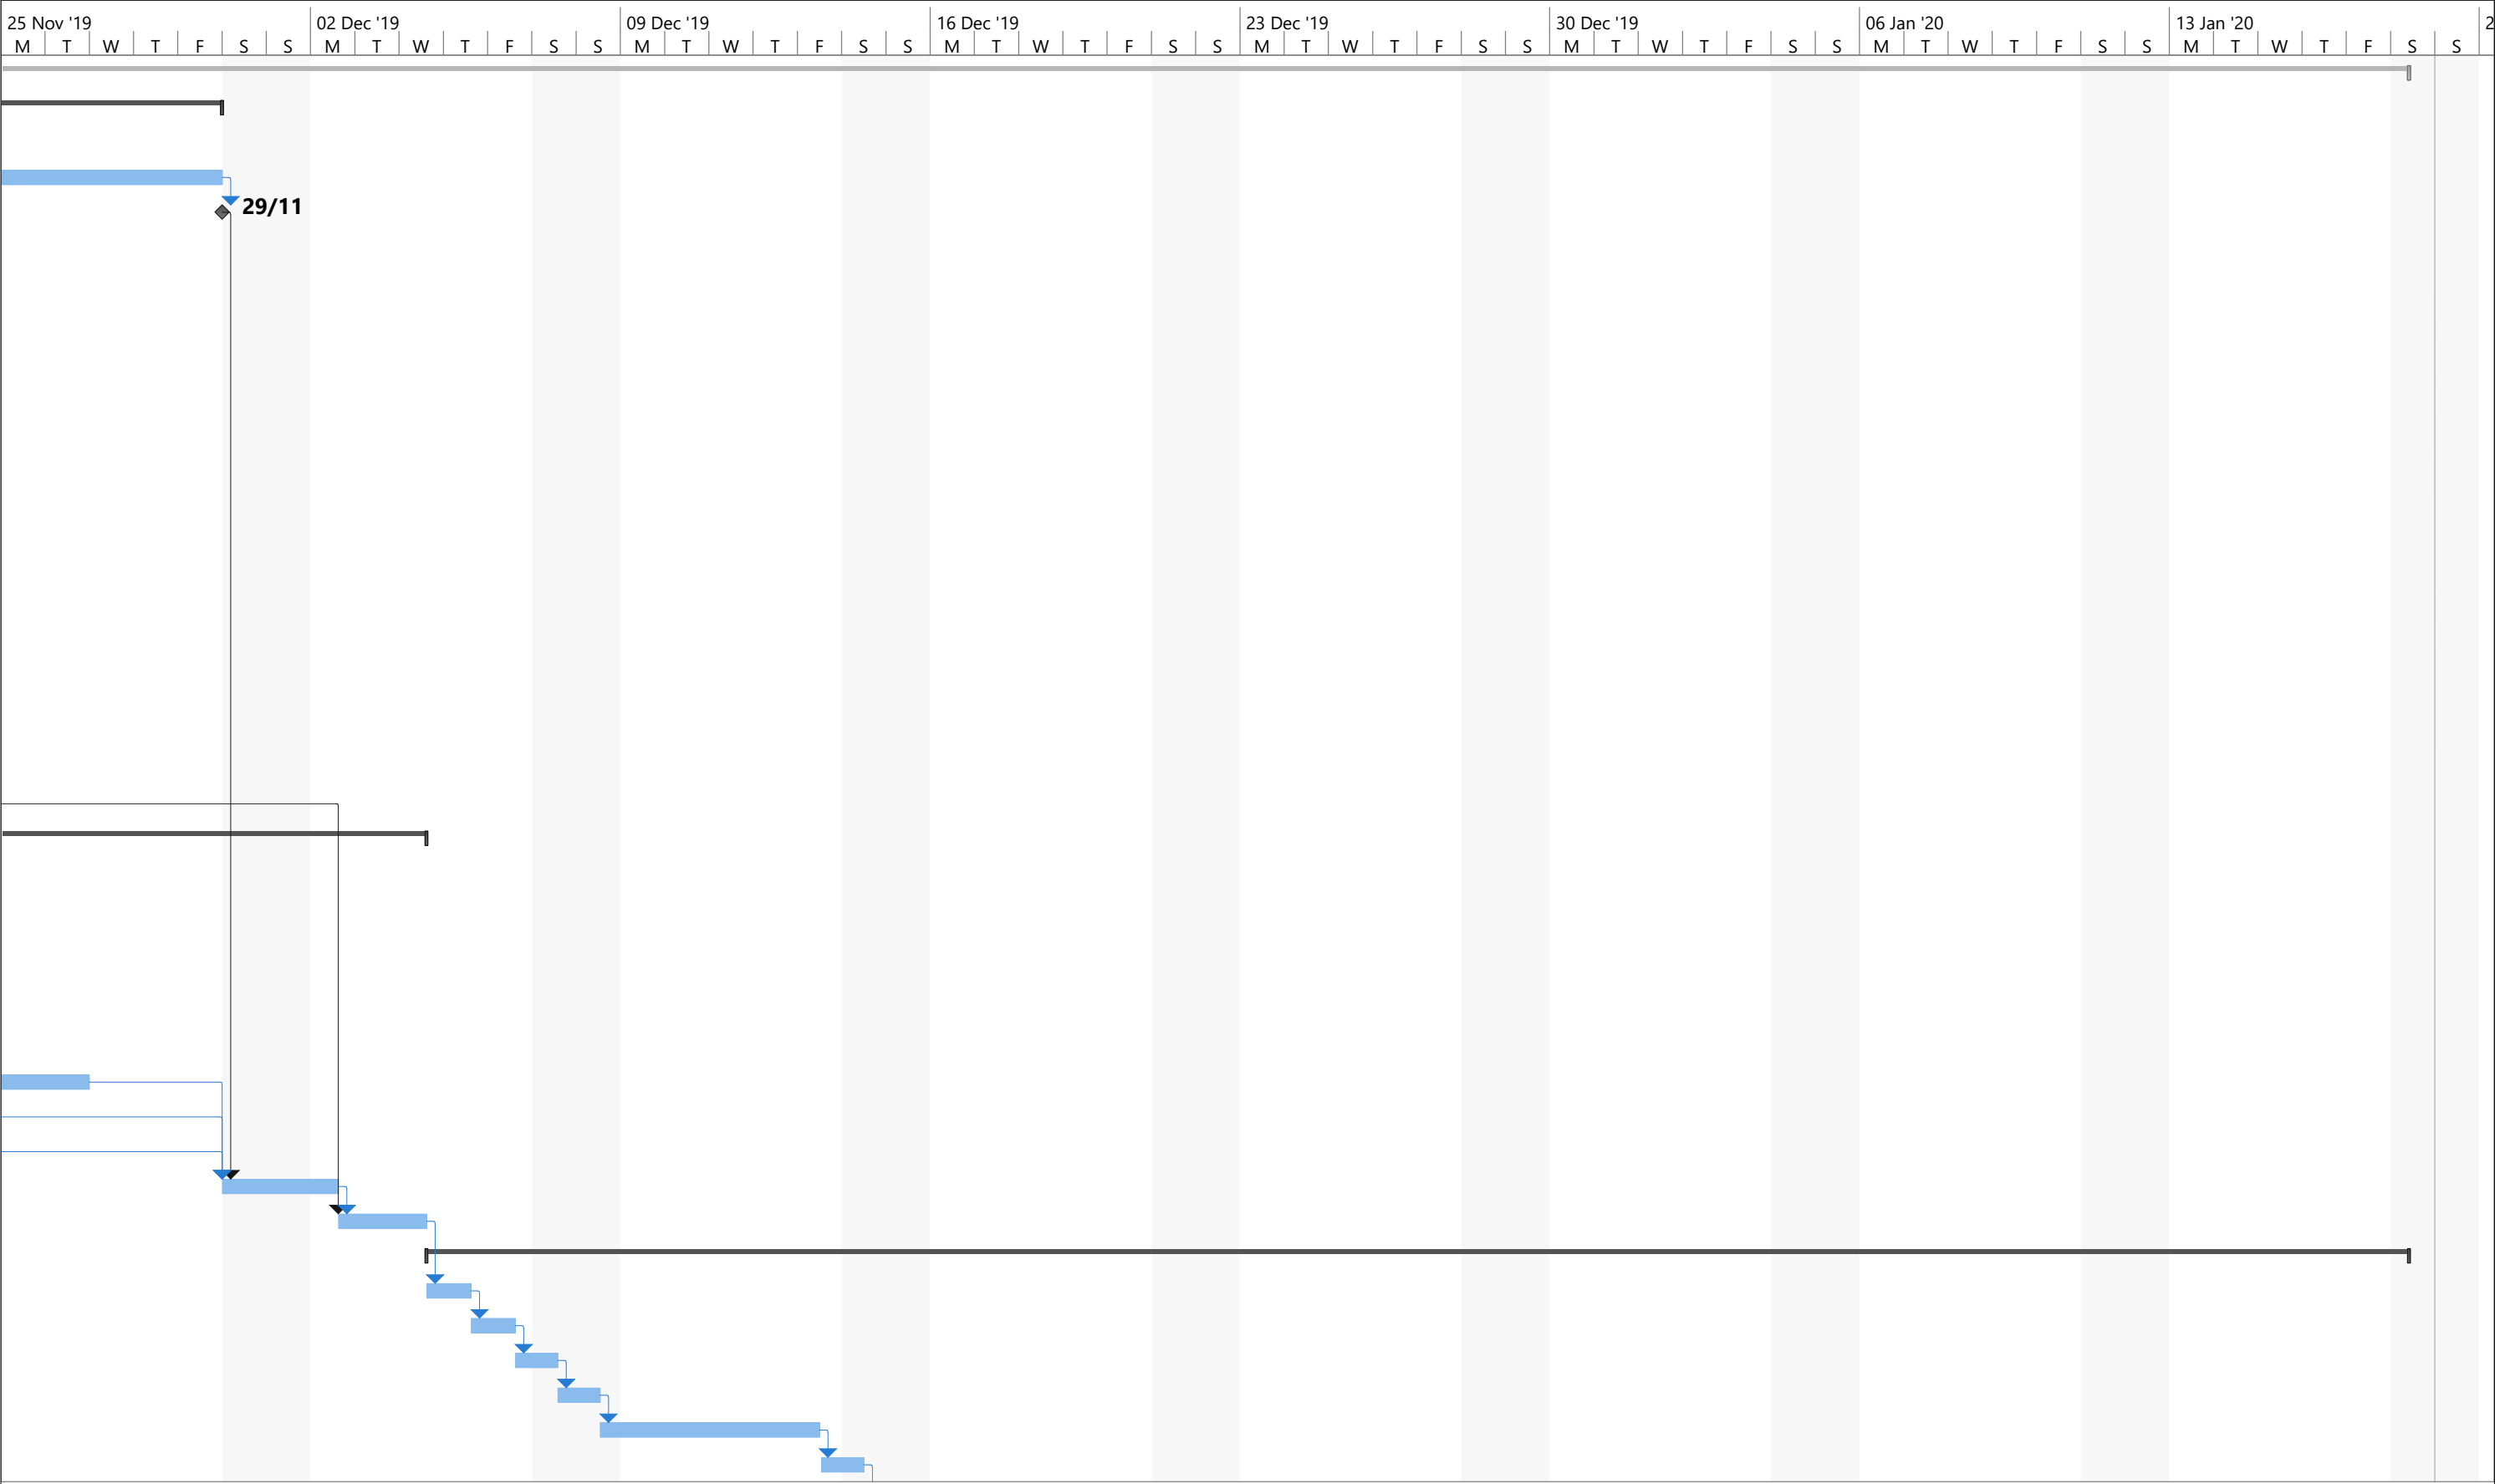

Project: Soku Turbo Trays Insta  
Date: Wed 09/10/19

Task



Project Summary



Manual Task



Start-only



Deadline



Split



Inactive Task



Duration-only



Finish-only



Progress



Milestone



Inactive Milestone



Manual Summary Rollup



External Tasks



Manual Progress



Summary



Inactive Summary













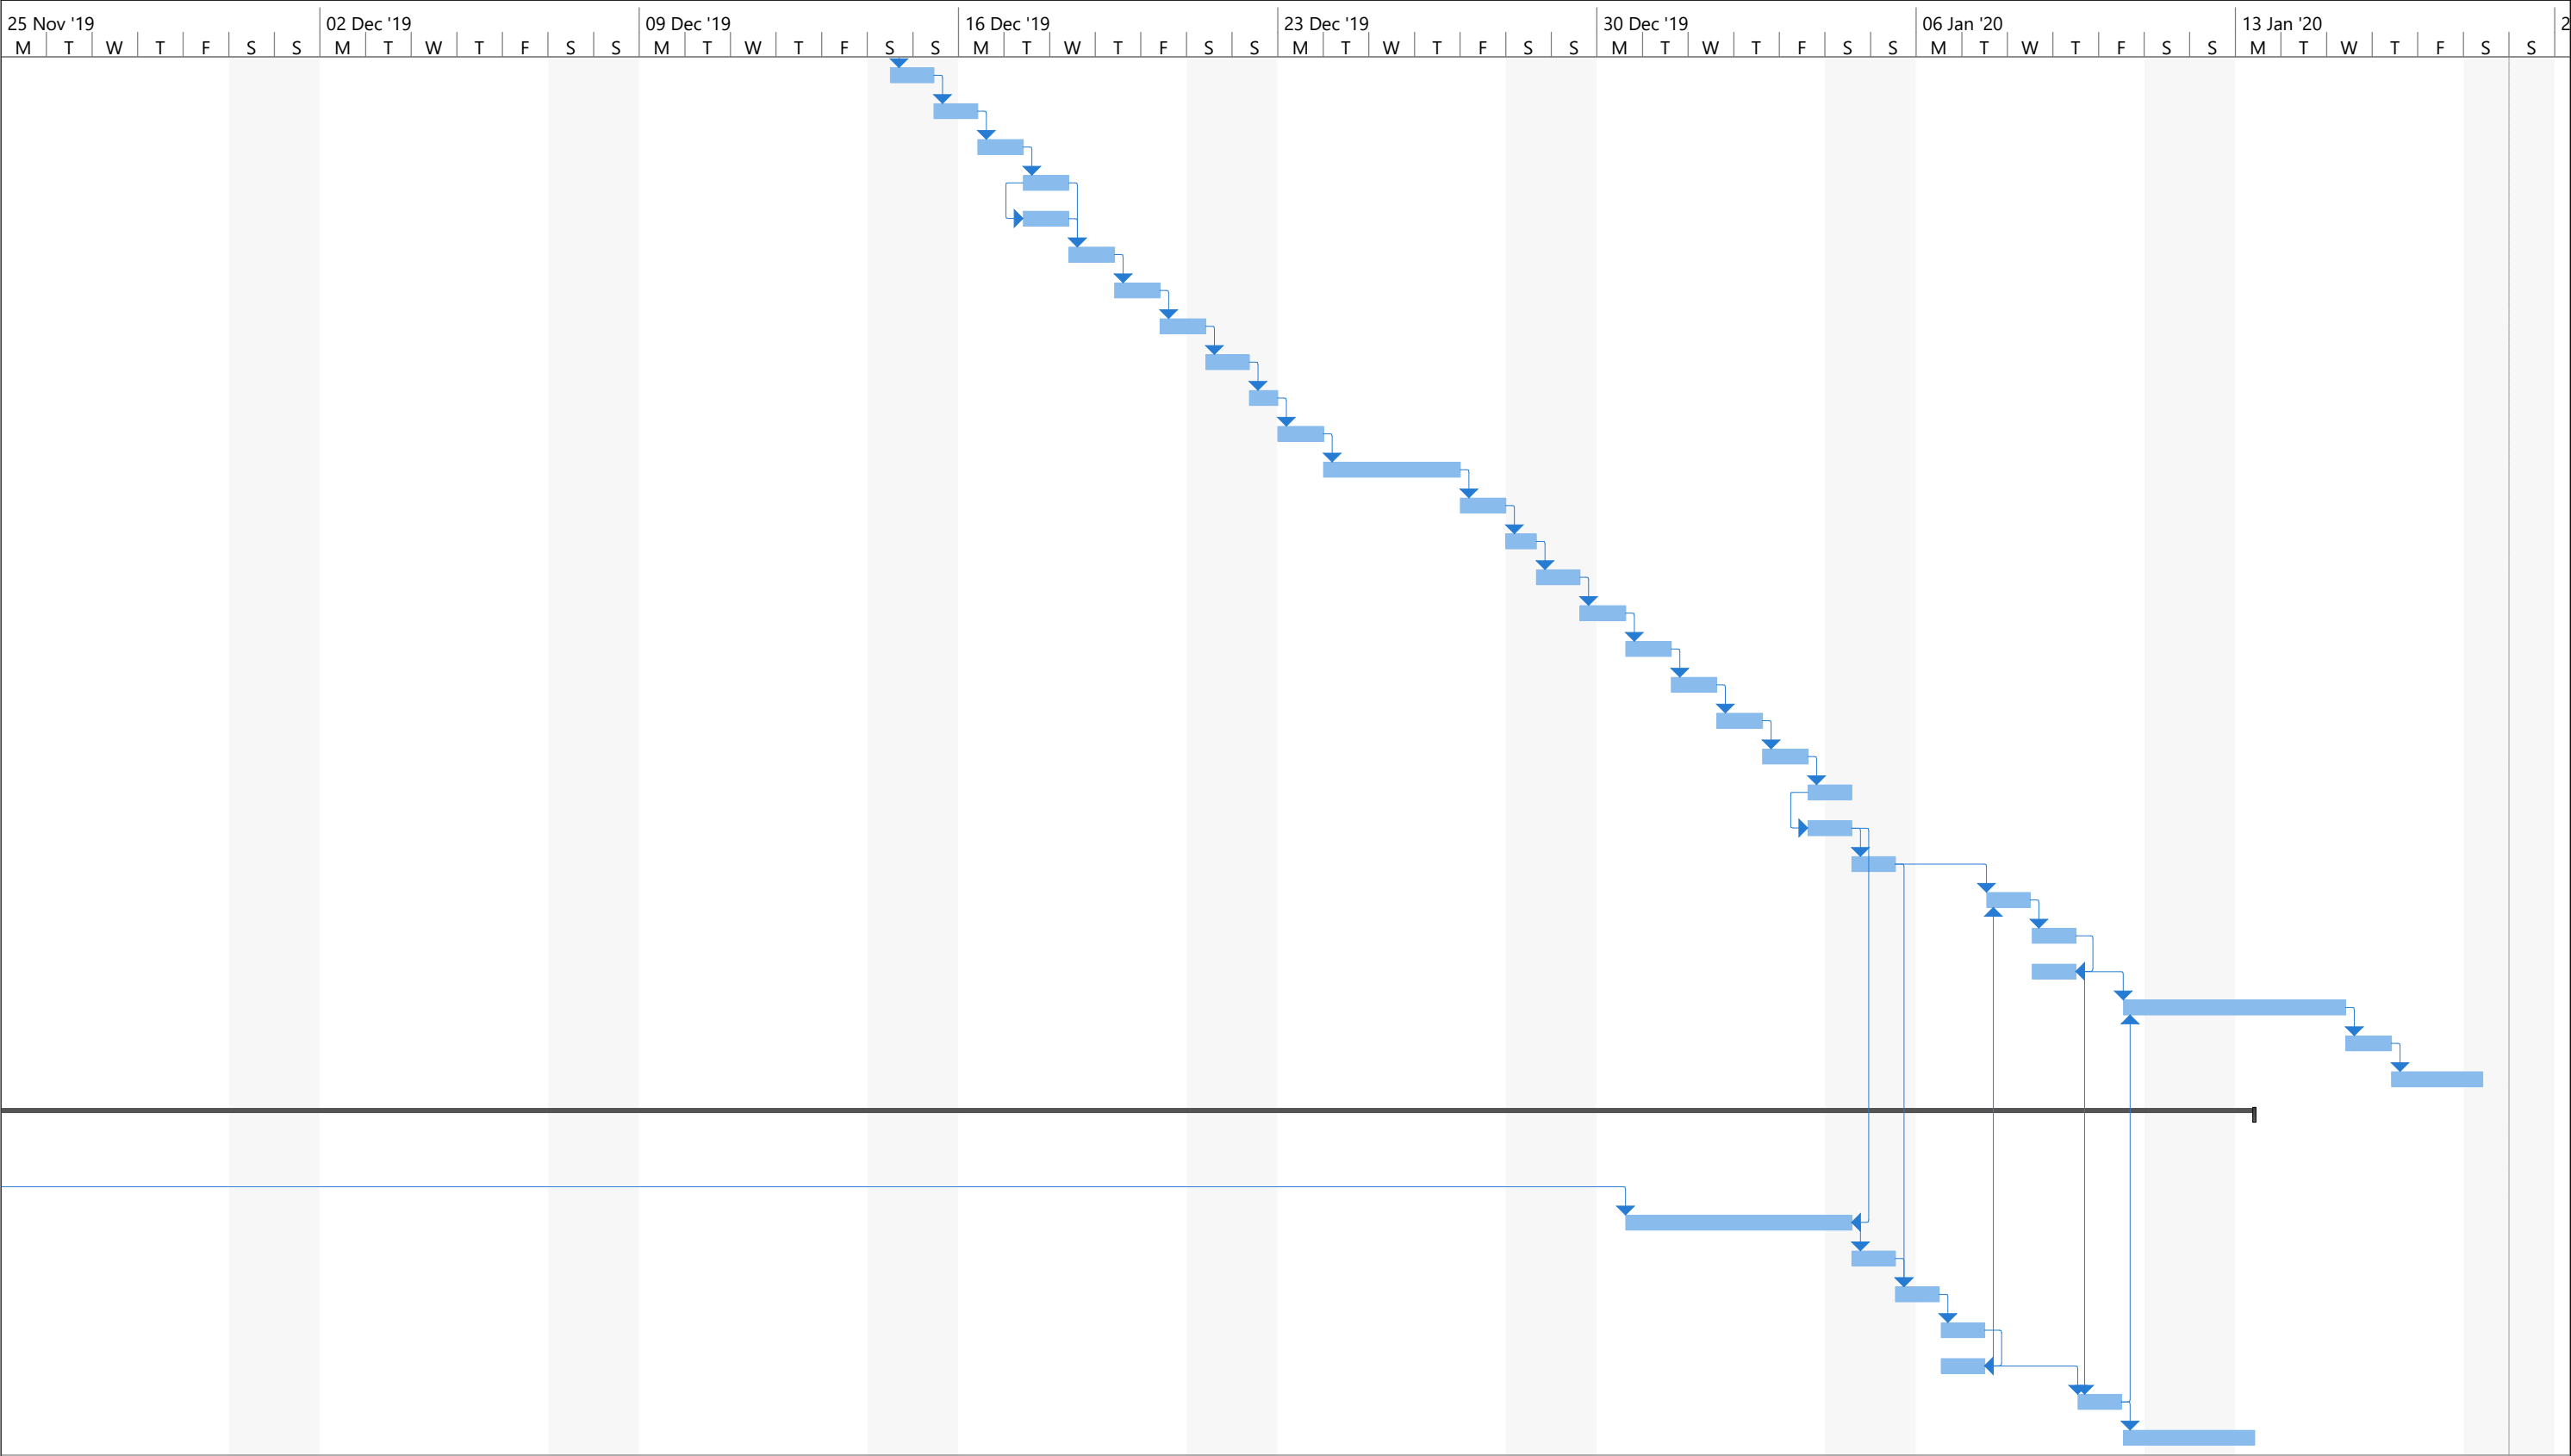








Manual Summary



External Milestone





Project: Soku Turbo Trays Insta Date: Wed 09/10/19	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone	
