


	Task Mode	Task Name	Duration	Start	Finish	Fri 05 Apr 01214161810121
--	-----------	-----------	----------	-------	--------	--

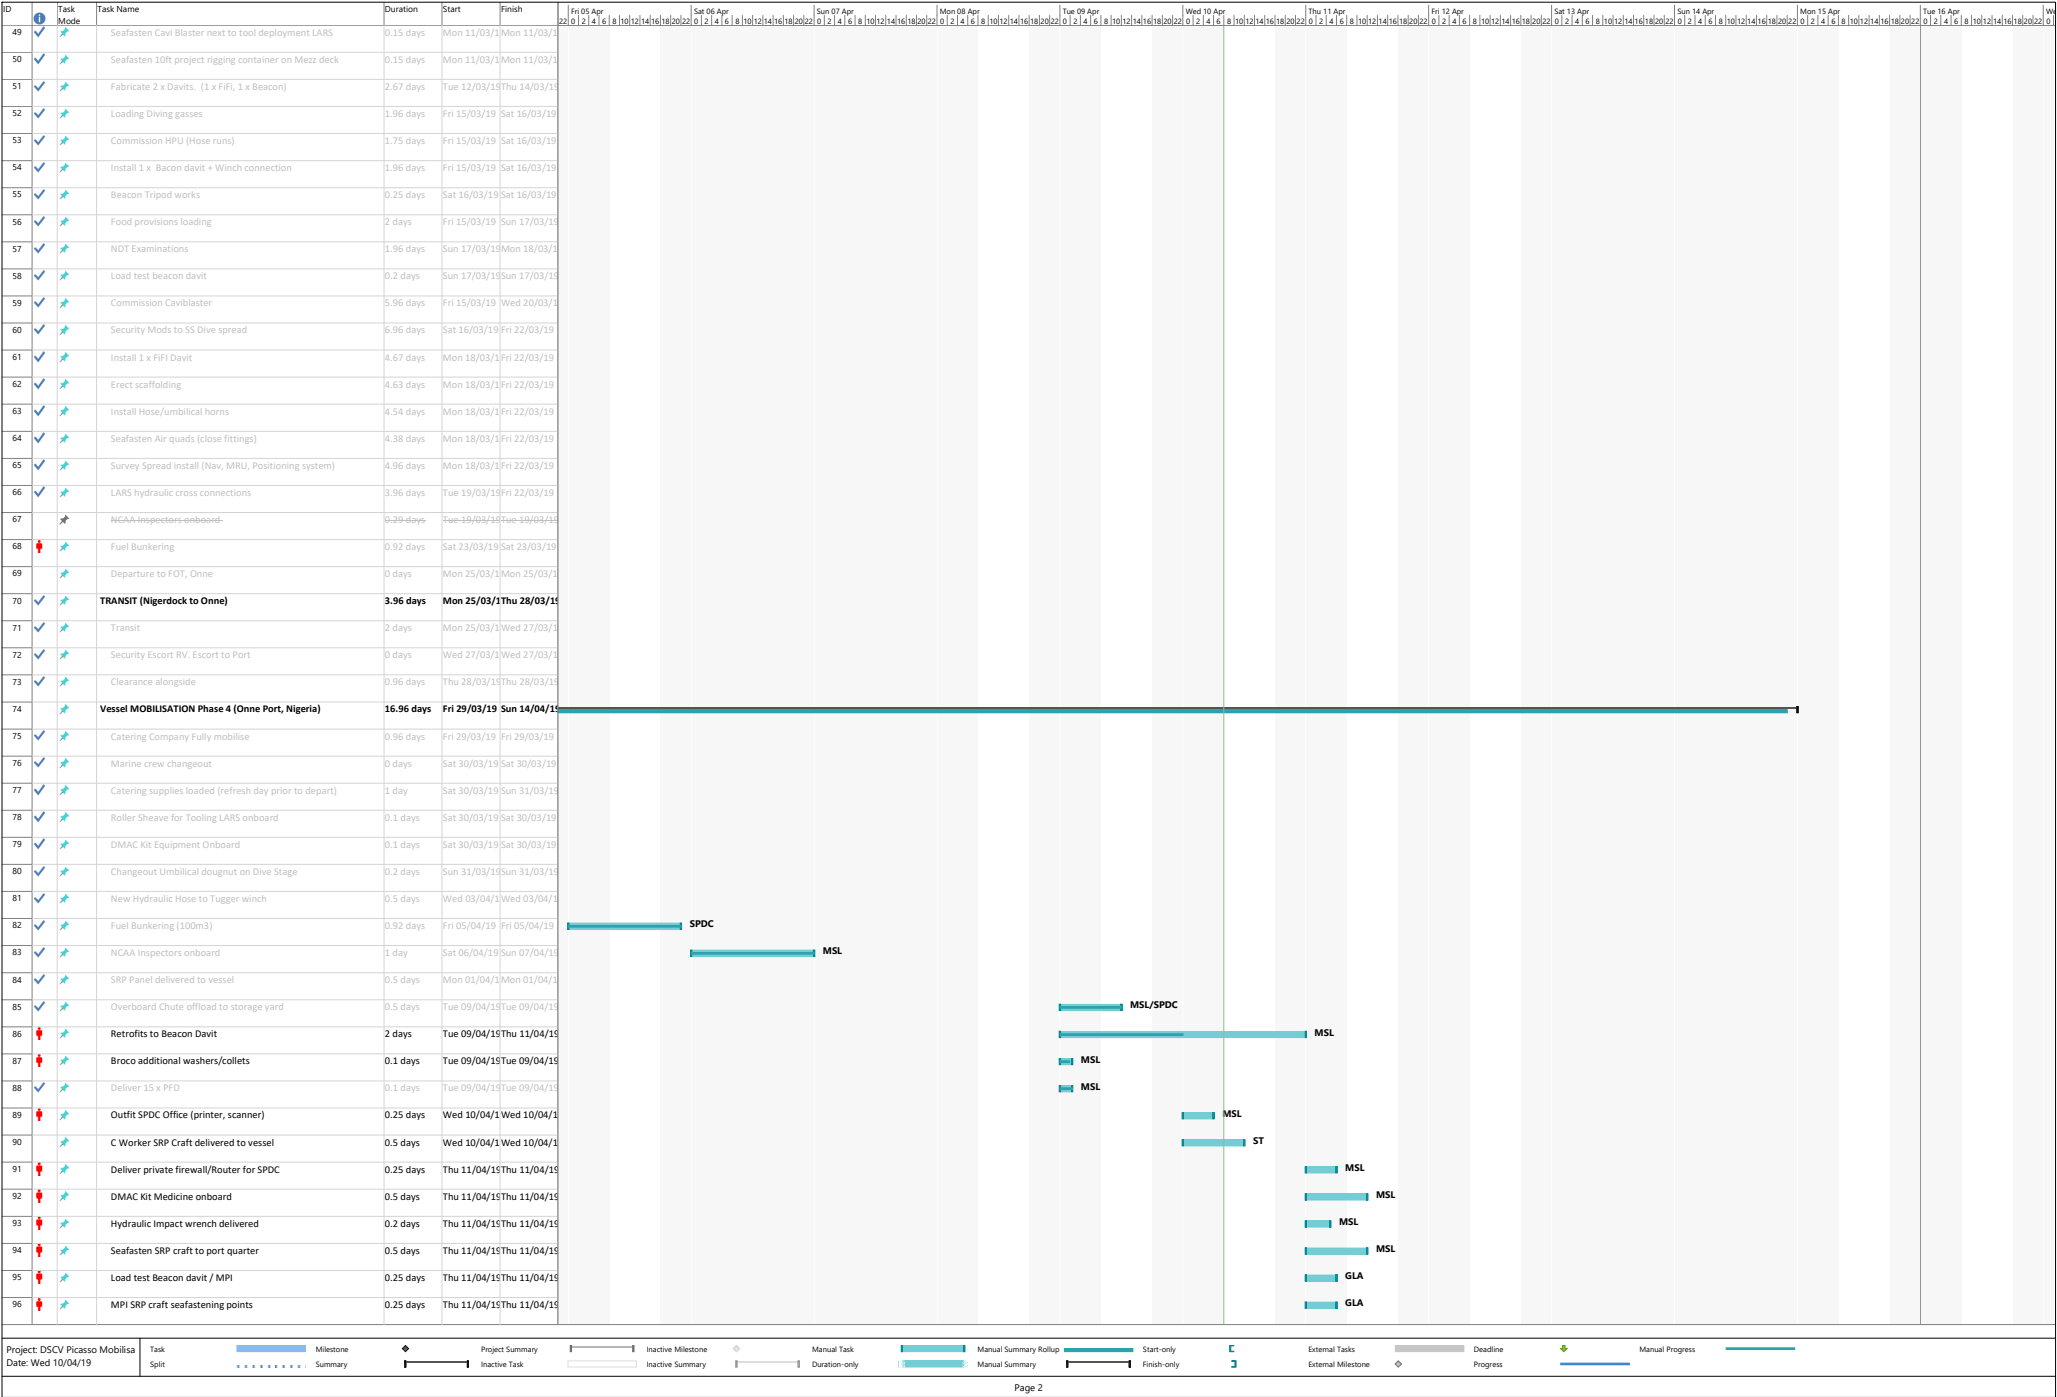

	Task Mode	Task Name	Duration	Start	Finish	Fri 05 Apr	Sat 06 Apr	Sun 07 Apr	Mon 08 Apr	Tue 09 Apr	Wed 10 Apr	Thu 11 Apr	Fri 12 Apr	Sat 13 Apr	Sun 14 Apr	Mon 15 Apr	Tue 16 Apr
97	🔍	Load test 10ton Tugger	0.96 days	Thu 11/04/19	Thu 11/04/19								GLA				
98	🔍	Update CMID C-Worker	0.96 days	Fri 12/04/19	Fri 12/04/19								ST				
99	🔍	Current Meter onboard	0.1 days	Fri 12/04/19	Fri 12/04/19								MSL				
100	🔍	Additional mini beacons delivered	0.1 days	Fri 12/04/19	Fri 12/04/19								MSL				
101	🔍	RADAscan system onboard	0.1 days	Fri 12/04/19	Fri 12/04/19								MSL				
102	🔍	Back Flush Pump onboard	0.5 days	Sat 13/04/19	Sat 13/04/19									MSL			
103	🔍	Local content crew changeout	1 day	Sat 13/04/19	Sun 14/04/19									UDS			
104	🔍	Activate Bandwidth increase 2mb	1 day	Sat 13/04/19	Sun 14/04/19									UDS			
105	🔍	Fresh food topup	0.5 days	Sun 14/04/19	Sun 14/04/19										MSL		
106	🔍	Fuel Bunkering (750m3 plus)	0.92 days	Sun 14/04/19	Sun 14/04/19											SPDC	
107	🔍	Security Escort RV	0 days	Sun 14/04/19	Sun 14/04/19											14/04	
108	🔍	Drills / Lock down	0.5 days	Sun 14/04/19	Sun 14/04/19											UDS	
109	🔍	Departure from FOT	0 days	Sun 14/04/19	Sun 14/04/19											14/04	
110	🔍																
111	🔍																
112	🔍																
113	🔍	DOCUMENTATION MOBILISATION	44.96 days	Fri 01/03/19	Sun 14/04/19												
114	🔍	HSEQ Bridging Documentation	71.96 days	Fri 01/02/19	Sat 13/04/19											MSL,UDS,SUBTECH	
115	🔍	Diving Equipment / PMS Bridging Document	43.96 days	Fri 01/03/19	Sat 13/04/19											MSL/Subtech,UDS	
116	🔍	Dive Tech Letter of Appointment	0.96 days	Wed 03/04/19	Wed 03/04/19												
117	🔍	Mobilisation Plan	43.96 days?	Fri 01/03/19	Sat 13/04/19											MSL/Subtech	
118	🔍	Diving Project Plan	43.96 days?	Fri 01/03/19	Sat 13/04/19											MSL/Subtech	
119	🔍	Project Procedure (Bonny, Forcados, OGG5)	43.96 days	Fri 01/03/19	Sat 13/04/19											MSL/Subtech	
120	🔍	Lift Plans (OGGS, SRP)	1 day	Mon 15/04/19	Tue 16/04/19												MSL/Subtech
121	🔍	Surface Umbilical Management Plan (SUMS)	37.96 days	Fri 01/03/19	Sun 07/04/19												MSL/Subtech
122	🔍	Emergency Response Plan	43.96 days	Fri 01/03/19	Sat 13/04/19												MSL/Subtech
123	🔍	HIRA Level 1	1 day	Sat 13/04/19	Sun 14/04/19												MSL/Subtech
124	🔍	HIRA Level 2 (offshore)		??	??												
125	🔍	Activity Specific Operating Guidelines (ASOG)	41.96 days	Fri 01/02/19	Thu 14/03/19												
126	🔍	IMCA Design 23	43.96 days?	Fri 01/03/19	Sat 13/04/19												MSL/Subtech
127	🔍	IMCA Design 40	43.96 days?	Fri 01/03/19	Sat 13/04/19												MSL/Subtech
128	🔍	FMEA for SRP															
129	🔍	NCAA Temp licence	61.96 days	Mon 11/02/19	Sat 13/04/19												MSL,UDS
130	🔍	Community relations (Bonny, forcados, OGG5)	62.96 days	Sun 10/02/19	Sat 13/04/19												MSL,UDS
131	🔍	OSP Permits for joining crew (Helicopter transfers)	43.96 days	Fri 01/03/19	Sat 13/04/19												MSL,UDS
132	🔍																
133	🔍	PERSONNEL MOBILISATION (Dive team)	39.96 days	Wed 06/03/19	Sun 14/04/19												
134	🔍	Miden CSR	0 days	Fri 15/03/19	Fri 15/03/19												
135	🔍	Dive Superintendent	0 days	Sat 13/04/19	Sat 13/04/19												13/04
136	🔍	Dive Supervisor	0 days	Tue 19/03/19	Tue 19/03/19												13/04
137	🔍	Expat Diver (x 4)	0 days	Sat 13/04/19	Sat 13/04/19												13/04
138	🔍	National Divers (x4)	0 days	Sat 13/04/19	Sat 13/04/19												13/04
139	🔍	Shell CSR	0 days	Thu 14/03/19	Thu 14/03/19												
140	🔍	HSE officer	0 days	Sat 13/04/19	Sat 13/04/19												13/04
141	🔍	Medic / Nurse	0 days	Sat 13/04/19	Sat 13/04/19												13/04
142	🔍	Lifting AP	0 days	Sat 13/04/19	Sat 13/04/19												13/04
143	🔍	Riggers (x2)	0 days	Sat 13/04/19	Sat 13/04/19												13/04
144	🔍	Surveyors (x2)	0 days	Sat 13/04/19	Sat 13/04/19												13/04

Project: DSCV Picasso Mobilisa
Date: Wed 10/04/19

Task Split

Milestone Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 3
